




DAS TECHNOLOGY

Customer Data Platform

TECHNICAL PROPOSAL

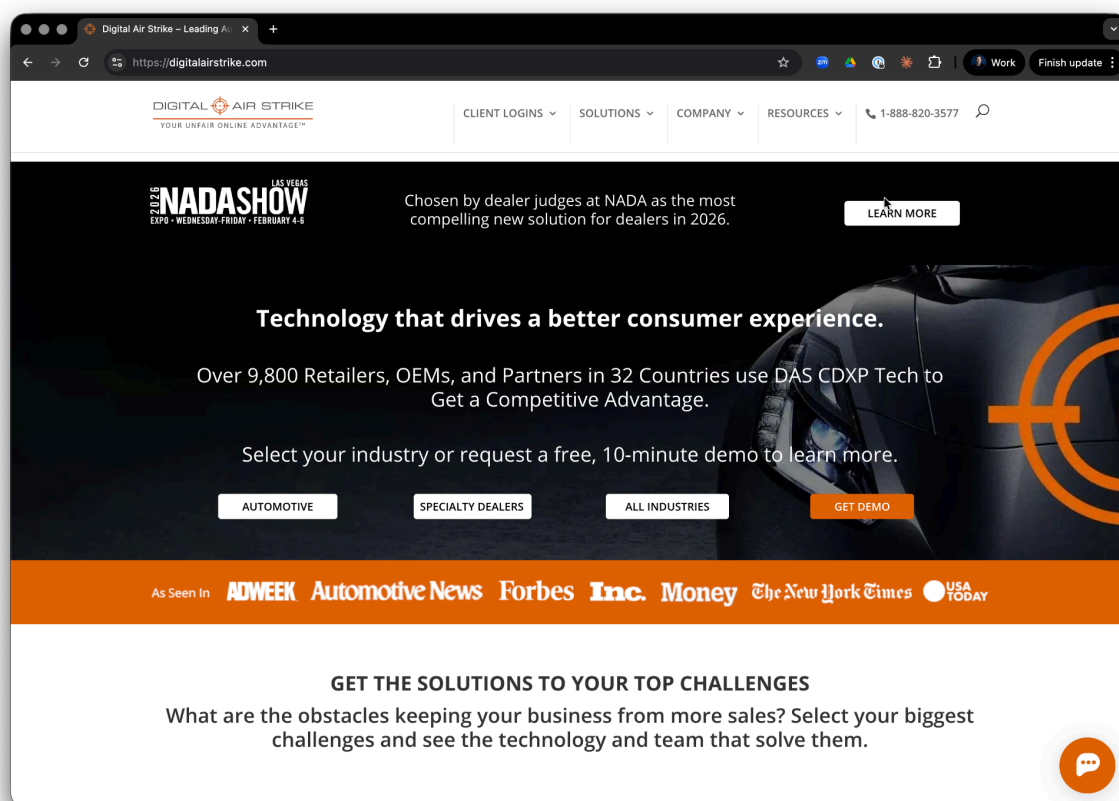

Prepared for: Dan Aston | DAS Technology (Digital Air Strike)

Prepared by: Conflict

Date: March 2026



DAS TECHNOLOGY — CUSTOMER DATA PLATFORM

Overview

DAS has consumer and vehicle data scattered across CRMs, DMS platforms, ad channels, and internal apps, with no unified view of who a customer is across dealerships. Every application you build downstream (including the Vehicle Smart Score) has to solve the same identity and data aggregation problem from scratch.

A CDP fixes this at the root. One system that ingests data from every source, resolves it to a single consumer identity, stores it clean, and exposes it via API to anything that needs it.

The DAS team has done significant upfront work spec'ing the architecture and data model. We've reviewed the MVP Specification (v4), Architecture Plan (v3), VSS Spec (v2), and the data mapping. What follows is our recommended approach, informed by the specs provided, grounded in what we've built before for similar use cases.

What We Know

From our March 9 discussion and the materials shared:

- **27 core data points** across 5 categories (vehicle/owner, service/parts, service history, vehicle protection, equity/insurance) define the initial data model, but these are the core of a much larger picture
- **100+ data sources** across leads, sales, service, vehicle, media, and more feed into those core data points and beyond. The CDP needs to account for all of them, not just the 27, but the enrichment and context that surrounds them
- **Identity unification is the core problem:** consumers appear across 100+ sources with inconsistent identifiers, and you need a single golden record per Dealer-Customer. Solving identity resolution and data enrichment across this landscape is the #1 priority
- **Multi-tenant isolation** is non-negotiable, dealership data must be siloed, with DAS maintaining a global view
- **Multiple ingestion channels** are needed: real-time webhooks, event streams, bulk upload, and scheduled batch pulls from external systems
- The **VSS app is the first consumer** of CDP data, but the platform needs to serve future applications too
- **Microsoft Azure is the current infrastructure**, with existing DevOps and AKS capacity and **additional cloud presence in Amazon Web Services**
- DAS has already begun pulling data models from existing systems using internal tooling, there is have a solid starting point for the data source audit



Phase 0: Discovery & Scoping Engagement

What This Is

A fixed-scope engagement to map the real data landscape, solve for identity unification and data enrichment across 100+ sources, and deliver a concrete build recommendation before any infrastructure is provisioned or code is committed.

We've shared our technical response outlining implementation paths. This engagement grounds that document in DAS's actual data, systems, and constraints; and answers the questions the technical response can't.

Why Phase 0

The technical response covers *what* we'd build. Phase 0 answers the questions that determine *how*:

- What do the 100+ data sources actually look like? What formats, what quality, what gaps?
- How do the 27 core data points map to what's actually available and what enrichment lives beyond them?
- What does a unified Dealer-Customer record look like when you coalesce all of them?
- What are the reliable identity keys across sources? Where does identity break down?
- Which ingestion channels matter first? Which can wait?
- What does DAS's existing infrastructure look like and what constraints does it impose?
- What's the right scope for the first build phase and what's the right stack to build it in?

Building without answering these could consume weeks. This engagement answers those questions in writing; a revised architecture plan, a privacy-by-design framework, an identity graph plan, and detailed Phase 1 & 2 plans; so the next SOW can be fixed-scope with confidence.

Team

A small, senior team working closely with DAS for the duration of the engagement. This is the same team that would carry the work forward into a build phase; discovery isn't handed off to a separate group. What they learn here informs what they build later.

Role	Focus
Solutions Architect (x1)	System design, data modeling, identity resolution strategy, path recommendation
Platform Specialist (x1)	Infrastructure evaluation, deployment topology, cloud constraints, observability, and system topology
Senior Engineers (x2)	Data source mapping, schema validation, ingestion channel analysis, spike prototyping

Scope

This is a fixed-scope, fixed-fee engagement. The weekly breakdown below is guidance, work takes as long as it takes. The team ramps up and engages as needed across the month. If discovery converges early, we can shift into productive work, prototyping data transformations, spiking identity resolution, scaffolding schemas.

Weeks 1–2: Discovery

- **Stakeholder interviews:** Walk through the technical response with DAS engineering, product, and data teams. Validate priorities. Surface unknowns.
- **Data source audit:** Starting from Dan's existing data model exports, catalog the 100+ sources across leads, sales, service, vehicle, media, etc. For each: what system owns it? What format (API, DB, file, event)? What fields identify a customer? What's the field-level mapping to a unified Dealer-Customer record?
- **Data quality assessment:** Sample data from priority sources. Evaluate completeness, consistency, duplication rates, normalization needs.
- **Identity landscape:** How are consumers identified across DAS systems today? What identifiers are reliable? Where are the conflicts? What's resolvable with deterministic rules vs. what eventually needs ML? This is the #1 question the engagement needs to answer.
- **Infrastructure inventory:** Current cloud footprint, existing services, team familiarity, security/compliance constraints, CI/CD maturity.
- **Integration mapping:** CRM, DMS, Meta, TikTok, OEM feeds; what's available now vs. what's on the roadmap? Authentication methods, rate limits, data freshness.

Week 3: Analysis & Architecture

- **CDP definition:** What does the unified Dealer-Customer record actually look like across 100+ sources? Finalize the data model against real source data. Flag fields that need transformation, sources that aren't ready yet, data that should be added.
- **Identity resolution strategy:** Deterministic matching tiers, key hierarchies, conflict handling rules. Honest assessment of what's rules-based vs. what needs ML down the road.
- **Ingestion channel prioritization:** Rank channels by immediate value and source readiness. Recommend a phased rollout order.
- **Path recommendation:** Evaluate technology and infrastructure options against DAS's actual constraints: team skills, existing infra, timeline pressure, Phase 2 ambitions, operational preferences.
- **Risk register:** Data gaps, integration blockers, timeline risks, dependency risks; identified and ranked.

Week 4: Recommendation & Deliverable

- **Synthesize findings** into the CDP Scoping Document
- **Build estimate:** Stage-by-stage timeline for the recommended path, informed by real complexity rather than assumptions
- **Options matrix:** If the path isn't clear-cut, 2–3 scoped options with trade-offs and timelines
- **Build-ready backlog:** If DAS proceeds, the scoping document converts directly into build tasks



Deliverables

The following are the goals guiding this engagement. Periodic (weekly/bi-weekly) check-ins keep DAS informed and in control. CONFLICT will provide DAS with the following documentation at the end of the engagement as deliverables:

1. **Executive Summary:** A concise summary of the engagement findings, proposed solution, recommended scope, and implementation roadmap.
2. **Revised CDP Architecture Plan:** A revised version of the architecture document shared by DAS, rewritten by CONFLICT to reflect findings from the data source audit, identity landscape review, and infrastructure inventory. This will include:
 - a. Target-state data flow
 - b. Services topology
 - c. Deployment architecture
 - d. Alignment with DAS's current cloud footprint
3. **DAS CDP Roadmap:** A detailed data and technical proposal outlining the recommended path forward for DAS's CDP implementation. This roadmap will include the following components:
 - a. **CDP Scoping Document:** written report covering data source mappings, unified Dealer-Customer data model, integration analysis, infrastructure assessment, and risk register. This document will be structured so it can convert directly into a prioritized task backlog if DAS proceeds.
 - b. **Privacy-by-Design Framework for Dealer Data:** Tenant isolation model, dealer data segregation rules, consent and access boundaries, PII handling patterns, and audit/lineage requirements, designed for the dealer-tenant context specifically, not generic compliance boilerplate.
 - c. **Identity Resolution Strategy & Identity Graph Plan:** Deterministic matching tiers, key hierarchies, data conflict resolution rules, and the identity graph data model that coalesces consumers across 100+ sources into a single Dealer-Customer record. Honest delineation of what's rules-based vs. what eventually requires ML.
 - d. **Detailed Phase 1/2 Plans:** Stage-by-stage scope, sequencing, dependencies, and effort estimates for Phase 1 (foundational CDP + first ingestion channels + VSS consumer) and Phase 2 (expanded source coverage + advanced identity + downstream applications). Detailed enough to support a fixed-scope SOW for either phase.

What This Is Not

- An open-ended retainer or staff-augmentation arrangement, this is a defined scope with a defined fee.
- A commitment to build; that's a separate conversation informed by this work
- No infrastructure provisioned, no application code committed, no cloud accounts created

This is a fixed engagement. At the end, DAS has a series of documents, a recommendation, and options forward. The decision to build, and with whom, is entirely DAS's.



Outcome

At the end of Phase 0, DAS has:

1. **A CDP definition & roadmap:** What the unified Dealer-Customer record looks like across 100+ data sources, grounded in real data, not assumptions.
2. **An identity resolution strategy:** How to coalesce customer identity across systems, what's deterministic, what needs ML, and what the architecture looks like.
3. **A build recommendation:** Stack, infrastructure, phasing, and timeline; justified by what we learned, not by what we assumed going in.
4. **A running start:** If DAS proceeds to build, the scoping document is the spec. No discovery redo. Week 1 of build is week 1 of building.
5. **A team that is ramped:** The same team that performed discovery has built deep context on DAS's data, systems, and constraints; meaning phase 1 and beyond start with full velocity rather than a learning curve.

TIMELINE & INVESTMENT

Timeline

3–4 weeks is the likely duration. Scope can shift as we learn more; the time box is guidance, not a hard boundary. Work takes as long as it takes.

Stages	Discovery & Sessions	Documentation
Phase 0: Discovery & Scope	~2–3 weeks	~1-2 week

Delivery Team

Role	Focus
Lead Software Architect	System design, services architecture, integration patterns
Lead Data Architect	Data modeling, identity resolution, schema design
Dir. of Operations (Technical Lead)	Engagement leadership, architectural guidance, executive alignment
Platform Specialist	Infrastructure evaluation, deployment topology, cloud constraints
Senior Engineer	Data source mapping, schema validation, ingestion analysis, prototyping
